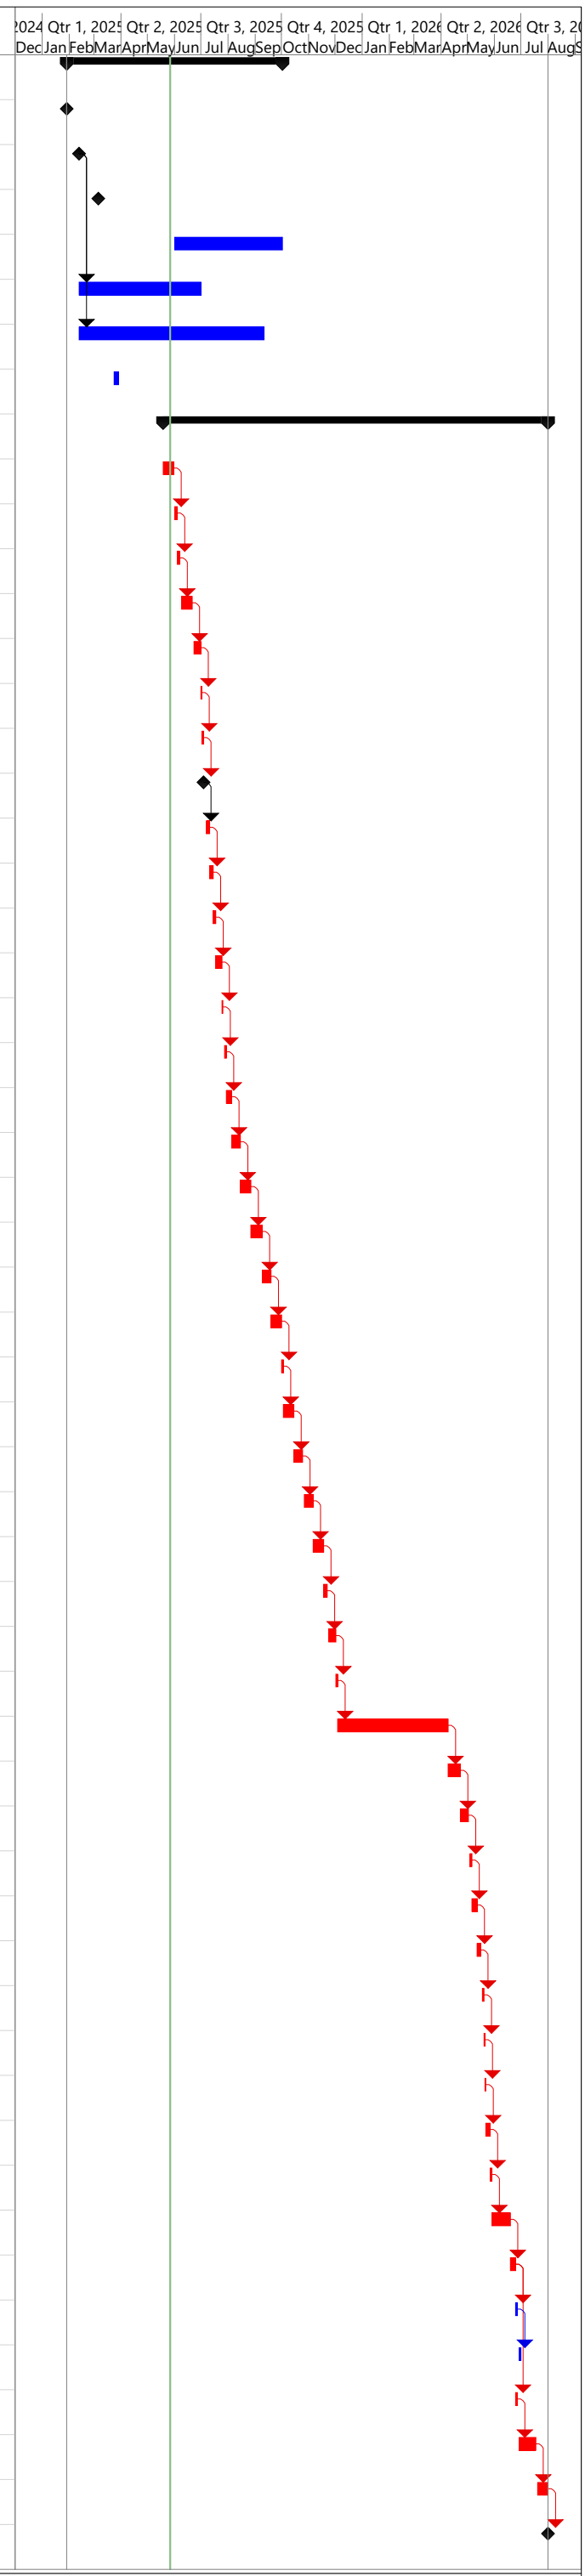ID	Task Name	Duration	Start	Finish
1	**Critical Project Dates**	**175 days**	**Wed 1/29/25**	**Wed 10/1/25**
2	Bid Date	0 days	Wed 1/29/25	Wed 1/29/25
3	Project Award	0 days	Wed 2/12/25	Wed 2/12/25
4	Preconstruction Meeting	0 days	Thu 3/6/25	Thu 3/6/25
5	In-Water Work Window	87 days	Sun 6/1/25	Wed 10/1/25
6	Design of Superstructure	100 days	Wed 2/12/25	Mon 6/30/25
7	Other project submittals	150 days	Wed 2/12/25	Wed 9/10/25
8	Clearing operations	5 days	Mon 3/24/25	Fri 3/28/25
9	**Bridge Construction**	**312 days**	**Mon 5/19/25**	**Fri 7/31/26**
10	Mobilization / site setup	10 days	Mon 5/19/25	Fri 5/30/25
11	Install / modify traffic control devices	3 days	Sun 6/1/25	Tue 6/3/25
12	Install project specific erosion control devices	3 days	Wed 6/4/25	Fri 6/6/25
13	Install temp detour approaches	10 days	Mon 6/9/25	Fri 6/20/25
14	Install temp detour bridge	6 days	Mon 6/23/25	Mon 6/30/25
15	Pave temp detour	1 day	Tue 7/1/25	Tue 7/1/25
16	install channelizing devices (barrier)	2 days	Wed 7/2/25	Thu 7/3/25
17	Activate temp detour	0 days	Thu 7/3/25	Thu 7/3/25
18	Remove existing temp bridge	4 days	Mon 7/7/25	Thu 7/10/25
19	Remove pavement and railings	2 days	Fri 7/11/25	Mon 7/14/25
20	Install containment under bridge	3 days	Tue 7/15/25	Thu 7/17/25
21	Demolish existing superstructure	5 days	Fri 7/18/25	Thu 7/24/25
22	Remove containment	1 day	Fri 7/25/25	Fri 7/25/25
23	Install cofferdams (channelize resource)	2 days	Mon 7/28/25	Tue 7/29/25
24	Demolish existing abutments	4 days	Wed 7/30/25	Mon 8/4/25
25	Excavate to ledge for new substructure	8 days	Tue 8/5/25	Thu 8/14/25
26	Form & place seal concrete - Abutment 1	8 days	Fri 8/15/25	Tue 8/26/25
27	Form & place seal concrete - Abutment 2	8 days	Wed 8/27/25	Mon 9/8/25
28	Form & place footing concrete - Abutment 1	8 days	Tue 9/9/25	Thu 9/18/25
29	Form & place footing concrete - Abutment 2	8 days	Fri 9/19/25	Tue 9/30/25
30	Remove cofferdams	2 days	Wed 10/1/25	Thu 10/2/25
31	Form and place breast wall concrete - Abutment 1	8 days	Fri 10/3/25	Tue 10/14/25
32	Form & place wing wall concrete - Abutment 1	8 days	Wed 10/15/25	Fri 10/24/25
33	Form & place breast wall concrete - Abutment 2	8 days	Mon 10/27/25	Wed 11/5/25
34	Form & place wing wall concrete - Abutment 2	8 days	Thu 11/6/25	Mon 11/17/25
35	Backfill abutment 1 to bridge seat	4 days	Tue 11/18/25	Fri 11/21/25
36	Backfill abutment 2 to bridge seat	4 days	Mon 11/24/25	Mon 12/1/25
37	Install NEXT Beams	2 days	Tue 12/2/25	Wed 12/3/25
38	Winter Shutdown	90 days	Thu 12/4/25	Wed 4/8/26
39	Form and place bridge deck	10 days	Thu 4/9/26	Wed 4/22/26
40	Form & place curbs	7 days	Thu 4/23/26	Fri 5/1/26
41	Install bridge rail	2 days	Mon 5/4/26	Tue 5/5/26
42	Common excavation in roadway	4 days	Wed 5/6/26	Mon 5/11/26
43	Install roadway gravel	4 days	Tue 5/12/26	Fri 5/15/26
44	Install approach rails (all 4 corners)	2 days	Mon 5/18/26	Tue 5/19/26
45	install guardrail where applicable	1 day	Wed 5/20/26	Wed 5/20/26
46	Install granite curb	1 day	Thu 5/21/26	Thu 5/21/26
47	Build sidewwalks (west side)	3 days	Fri 5/22/26	Tue 5/26/26
48	switch traffic onto new bridge (single lane - southbound)	2 days	Wed 5/27/26	Thu 5/28/26
49	Remove temporay bridge and approaches	15 days	Fri 5/29/26	Thu 6/18/26
50	General site grading / site stablization	4 days	Fri 6/19/26	Wed 6/24/26
51	Finish installing guardrail	2 days	Thu 6/25/26	Fri 6/26/26
52	Pave base on project	2 days	Mon 6/29/26	Tue 6/30/26
53	Pave surface on project	2 days	Thu 6/25/26	Fri 6/26/26
54	Finish contract items	15 days	Mon 6/29/26	Fri 7/17/26
55	Demobilize / clean up	10 days	Mon 7/20/26	Fri 7/31/26
56	Project complete	0 days	Fri 7/31/26	Fri 7/31/26
